

Jacobs Wells Baths Progress March 2026



Milestones completed

Truss repairs

Lantern removal


Asbestos decontamination

Pump room


South studio roof repair

Tanks stabilised

02: Pump Room - Decontamination:
Removal of all asbestos within Pump Room & decontaminate floor, retaining key existing features.

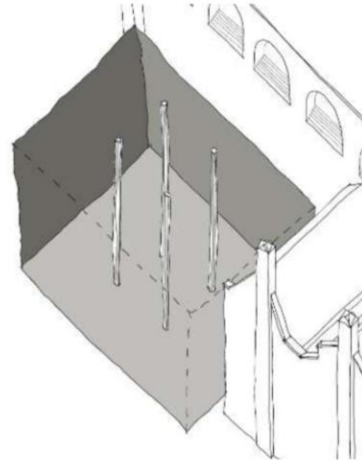


01 Boiler Room Parapet
Carefully dismantle prescribed, unsafe areas of boiler room parapet and store materials on site for future re-use.

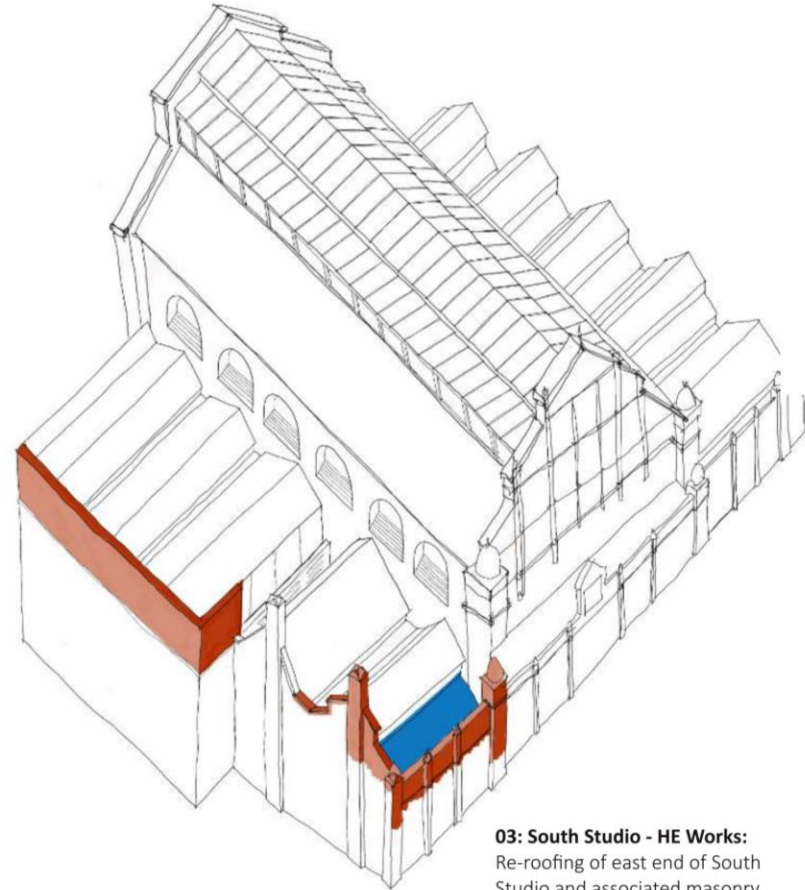

03: South Studio - HE Works:
Re-roofing of east end of South Studio and associated masonry repairs.

04: Tanks:
Drain tanks and repair as required for future use. Divert// stop up incoming supply.

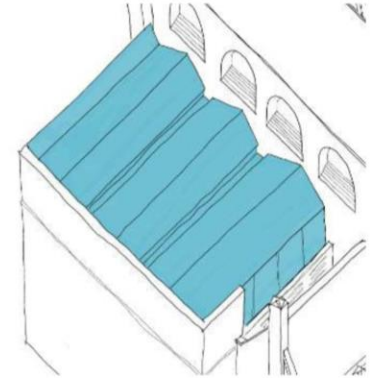

Main Hall

Internal scaffolding completed and tagged

Brickwork around metal trusses carefully dismantled for inspection


Embedded truss sections repaired and treated

Brick surrounds rebuilt following repairs

Internal roof stripped and high-level timber structure inspected

Lantern removal and full glazing replacement



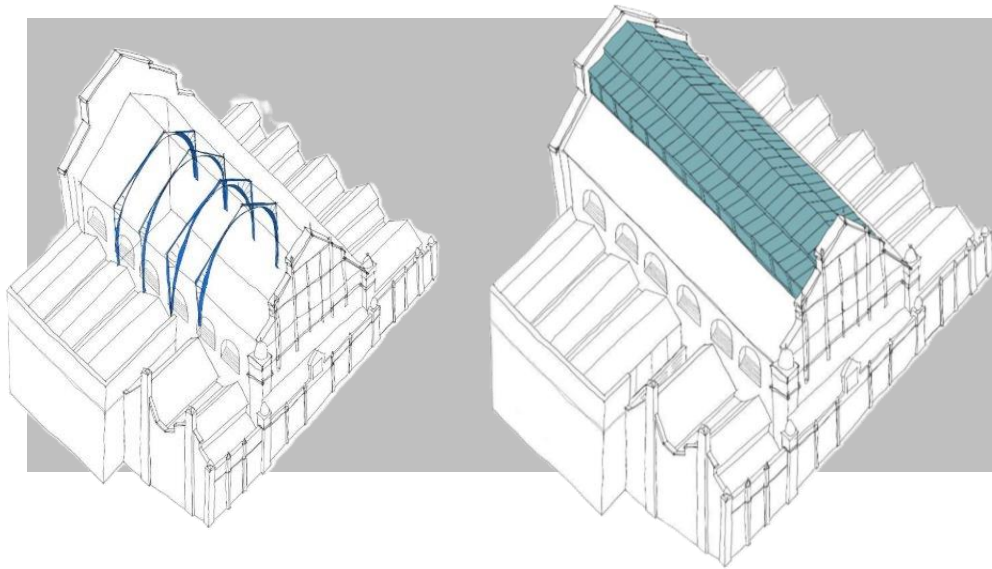

South Studio


Roof glazing and masonry
works completed

Temporary site office setup

Soft strip of internals

Space ready for site visits
and information point



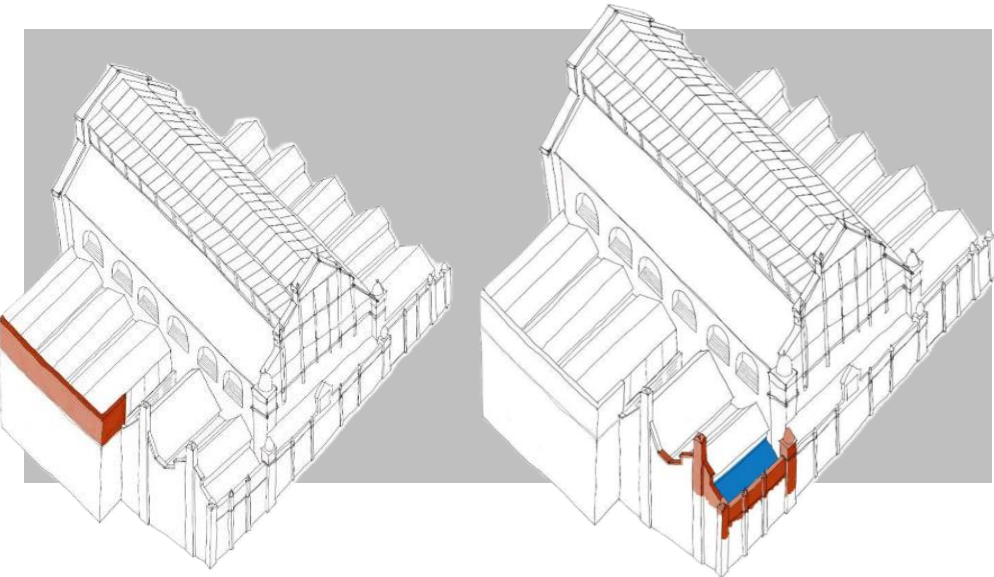

Pump Room

Temporary resurfacing completed to support works progressing as part of wider overall programme

Access enabled via internal scaffolding setup

Preparatory works aligned with structural inspections and sequencing






North Wing

Included within internal scaffolding and access strategy

Early-stage works coordinated alongside Main Hall activity

Further inspections and repair priorities to follow once full access confirmed



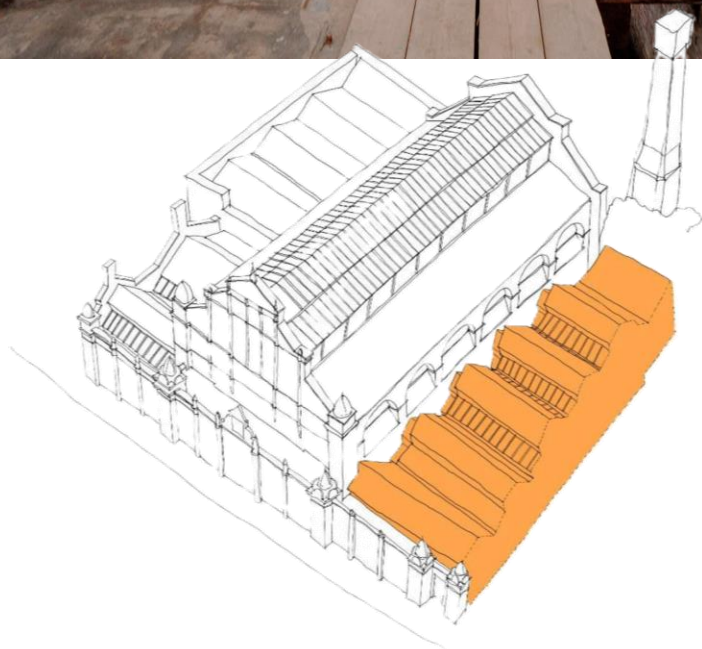

Masonry works

External scaffolding completion (Mar 2026)

Adaptations made for highways requirements and ground conditions (west elevation)

Installation of half-deck and all-weather covering to maintain programme


Asbestos-safe removal of rooflight glazing

Glazing replacement in progress

Masonry inspections scheduled with structural engineer and architect

Removal of vegetation and commencement of repointing and repairs



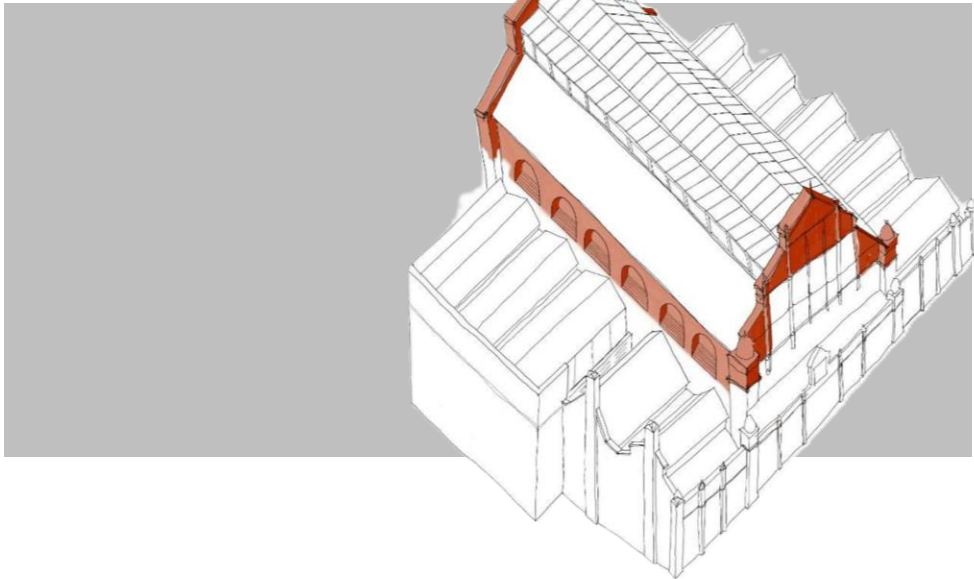

Art of the Possible

Creative activations on site feat artists Grove and Maneera (pic, right)

Learning & participation programme with artists, young people, uni students and local residents

Supporting new work, skills development and emerging talent

Builds pathways into creative careers alongside heritage learning and participation





Phase 2 What's Next



PROPOSED FRONT ELEVATION - scale 1:100 @ A1

Key Funders & Supporters

